FILL CHART

Material Location	Description	Material Classification		lassification	Compaction/Density Requirement (NOTE 3)
FINAL FILL Fill starting from the top of the embedment fill layer. (NOTE 1 and 2)	Suitable Fill Materials as noted in the Project Geotechnical Report and noted on the Site Design Engineer's Plans	See Project Geotechnical Report and Site Design Engineer's Plans		nnical Report and Site	Plate Compact or Static Roll up to 8-inch loose lifts to densify fill. Use at least two full passes of the equipment to level the layer. Continue until 24 inches of total fill thickness has been placed above the tank. For AASHTO M145 soils, a minimum of 95% of the Standard Proctor Maximum Dry Density is recommended. After 24 inches of fill is placed, place fill in accordance with the engineer of record's relative compaction requirement or to 95% of the Standard Proctor Maximum Dry Density - whichever is greater.
EMBEDMENT FILL Fill Immediately Surrounding the sides and top of tank (NOTE 4) BEDDING FILL Fill Immediately below the tank (NOTE 4)	Sand-Gravel Mixtures or Open-Graded Crushed Aggregate Blends	AASHTO M145 A-1, A-2-4, A-3	or	AASHTO M43	Plate Compact or Static Roll up to 8-inch loose lifts to densify fill. Use at least two full passes of the equipment to level the layer. For AASHTO M145 soils, a minimum of 95% of the Standard Proctor Maximum Dry Density is recommended.

NOTE 1: This layer can include pavement subbase

Cover Depth as

Specified By Site

Design Engineer

(See Cover Chart)

NOTE 2: If open-graded aggregates are used for embedment fill, fines migration from the final to embedment fill layer may be reduced by installing a layer of 6 oz non-woven geotextile fabric at the final and embedment fill interface.

-6 oz Non-Woven

Geotextile (outer) around

HD Side Panel (Part # 314062)

TYP. for all exterior sides

entire tank by Others

NOTE 3: See Construction Equipment Table for more information for construction equipment limitations.

NOTE 4: Import or native soils may be used if the soils meet the material classification listed. Fill material should be selected based on classification, groundwater conditions, and tank invert elevation

-Surface Material (Pavement Section

or Topsoil) as Specified by Site

Design Engineer


CONSTRUCTION EQUIPMENT CHART

Equipment Make (NOTE 1)	Maximum Gross Vehicle Weight (lbs)	Fill Depth over Tank (in)
Plate Compactor	1,500	6
Roller - Static Mode	12,000	18
Low Ground Pressure Tracked Vehicles (NOTE 2)	20,000	14
Roller - Vibratory Mode	12,000	24
Dump Trucks and Pans	NOTE,3	

NOTE 1: Vehicles shall make straight runs only across tank footprint.

NOTE 2: Maximum track pressure 7 psi for tracked vehicles.

NOTE 3: Dump trucks and pans shall not traverse or park over the system during construction. Backfill material may be temporarily unloaded near the excavation. Material shall not be stockpiled near the excavation for longer than 24 hours.



Remote Access Cover Vented (Part #314053)

-Concrete Load Distribution Plate by Others - See NOTE 2

Half-Layer Top Plate Cover

HD Half-Layer Side Panel (Part # 314095) TYP. for all exterior sides

HD Side Panel (Part # 314062)

TYP. for all exterior sides

(Part # 314094) TYP.

Remote Access Plate (Part

#314075) - See NOTE 3

or Solid (Part #314043) - See NOTE 1

-Extension Shaft (Part #314038)

COVER CHART

	Cover Thickness		
Live Loading Condition	Minimum	Maximum	
Non-Trafficked Areas (i.e.	12	124	
Landscaping)	12	134	
Passenger Vehicles Parking Lot			
(i.e. Gross Vehicle Weight	18	134	
<10,000 lbs)			
Passenger Vehicle Parking Lot			
with one weekly AASHTO HS-	20	134	
20 vehicle			
Heavy AASHTO HS-20 Traffic	22	134	
Passenger Vehicle Parking Lot			
with one weekly AASHTO HS-	24	134	
25 vehicle			
Heavy AASHTO HS-25 Traffic	26	134	


NOTE 1: Minimum Cover Thickness in non-trafficked areas is based on landscape surface with a 40 degree load distribution. In trafficked areas, Minimum Cover Thicknesses are based on an asphalt-surfaced pavement with a 30 degree load distribution. NOTE 2: Calculations assume backfill with a minimum 32-degree angle of internal friction and a maximum bulk density of 120 lbs per cubic foot, and a seasonal groundwater elevation at least 2 feet below the invert of the tank.

SIDE PANEL PIPE DIAMETER CHART

Inlet/Outlet Pipe Diameter		
Minimum	Maximum	
4 inches	18 inches*	

NOTE 1: Maximum pipe diameter directly into side panel is 15 inches. Remote access unit required for pipes larger than 15 inches.

NOTE 2: Cut inlet / outlet pipe hole prior to side panel installation. *NOTE 3: Contact ACO for guidance for inlet / outlet pipes larger

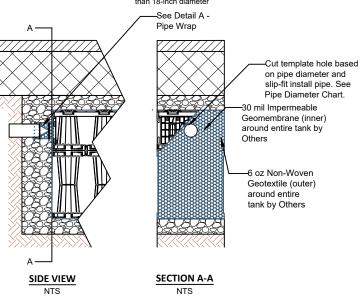

Engineer of Record

requirements during design and construction

responsible for checking

that subgrade soils meet

the bearing and settlement

Half-Layer Top Plate Cover

(Part # 314094) TYP.

(Part # 314095)

HD Half-Laver Side Panel

TYP. for all exterior sides

-FINAL FILL (See Fill Chart) -EMBEDMENT FILL (See Fill Chart)

-HD Half-Module (Part #314061) TYP.

-BEDDING FILL (See Fill Chart)

NOTE 1: The minimum width of sidewall backfill is 12" or large enough to accommodate selected compaction equipment, whichever is greater.

1.5 LAYER HD

INFILTRATION CROSS SECTION

1.5 LAYER HD ACCESS POINT CROSS SECTION

NOTE 1: Ventilation may be crucial to reducing the pressure build up within the system. If solid access covers are used, alternative methods of ventilation are recommended. NOTE 2: Concrete Load Plate not required for unpaved applications. Consult Engineer of Record for requirements

-HD Half-Module (Part #314061)

TYP. under access point

NOTE 3: The Remote Access Plate is approximately the size of half of a half-module. The half-module at the top of the tank must be cut in half to accommodate the Remote Access Plate

STORMBRIXX STANDARD DETAILS **HD SYSTEM - 1.5 LAYER - INFILTRATION**

WEST SALES OFFICE

CASA GRANDE, AZ 85122 Tel. (888) 490-9552 Fax (520) 421-9899

EAST SALES OFFICE 9470 PINECONE DRIVE

MENTOR, OH 44060 Tel. (800) 543-4764 Fax (440) 639-7235

Tel. (440)-639-7230 Fax (803)-802-1063

481 MUNN RD. SUITE #225

FORT MILL, SC 29715

www.acoswm.com

DRAWN BY A Frye	CHECKED BY J Jonke	
DATE	REV.	
04/26/2024	0	

ACO, INC. SOUTHEAST SALES OFFICE

1.5 LAYER HD

PIPE INSTALLATION
